

Work Order ID 163662

Wednesday, July 05, 2017 10:24:02 AM

163662

Page 1

Item ID: D350-748-201

Accept

N900040100

Setup Start

NS1

Revision ID:

Stop

NS2

Item Name: Aft Crosstube AS350 / AS355

Start Date: 7/5/2017 Start Qty: 1.00

1

Cust Item ID:

Required Date: 8/17/2017 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals:

Process Plan:

DAS
21

Date: JUL 05 2017

Tooling:

Date:

Run Start

NR1

QC:

DAS
9-89

Date:

SPC (Y/N):

Date:

Stop

NR2Sequence ID/
Work Center IDOperation
DescriptionSet Up/
Run Hours

Tool ID

Tool #

Plan
CodeAccept
QtyReject
QtyReject
NumberInsp.
Stamp

Draw Nbr

Revision Nbr

JUL 27 2017

DAS
6
9-89

D350-748-241

H

100

Document Control

0.00

100

DOCUMENT CONTROL

DC

Memo

0.00

Doc.Control -USB or Paperwork

Photocopy bluefile & type labels per PPPD350-748-201

CHG004

DAS
28
9-89

JUL 31 2017

110

1.69

110

BENDING MACHINE - CROSSTUBES

CNC Bend 2

Memo

0.83

CNC Alpha 160 Bender

Bend tube as per Dwg D350-748-241 using CNC bender program D350A and Folio FT

*****UNDER BEND .225" PER SIDE*****

****USE (4) DT9824 SHIM BLOC TO CHECK STRAIGHTNESS****

****VERIFY CROSSTUBE DIMENSIONS AS PER DWG****

 17 07-17

DQA:

Date: 2017-08-09



AUG - 2 2017 WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed:

Date:

Work Order update only ☐

Work Order: 163662 Part No. D370-744-201 NCR No. 17-6569		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☒ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Cross tube ☒ Water Jet ☐ Engineering ☐ Machining ☐ Small Fab ☐ Prod. Eng. Coord. ☐ Quality ☐ Thermoforming ☐ Finishing ☐ Rec/Store/Packaging ☐ Other ☐ Large Fab ☐ Composite ☐ Supplier ☐					
Date: 17/7/17		Step #: 110		QTY Effective: 1			MRB (QSI042) Approval LDAS 142 9-89 17/7/17		
Description Work Order Deviation				Disposition				Completed By DAS 12 9-89 17/7/17 Lead hand / Supervisor Approval Verification DAS 38 9-89 JUL 13 2017 QC / QA Coordinator Approval DAS 38 9-89 JUL 13 2017	
Tube is bent narrower, -0.26" total width vs nominal.				Acceptable. but unlikely to cause fit issues.					
Root Cause Environment ☐ No Re-verification ☐ Design ☐ Operator ☐ Doc/Data ☐ Offset/Setup ☐ Equip/Tooling ☐ Supplier ☐ Handling/Pre ☐ Training ☐ Material ☒ Use for Testing ☐ Internal Transport ☐ Poor Information ☐ Tribal Knowledge ☐ Rushing ☐ LOA ☐ Product Improvement ☐ Substation ☐ Process Improvement ☐ Past Expiry Date ☐ Manufacturing Process ☐ Misidentified ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Temperature/Cure ☐ Power Loss/Surge ☐ Positioned Wrong ☐ Bending ☐ Set-up ☐ Folio/Program ☐ Outside Dimensions ☐ Centre Not Concentric ☐ BOM/Route ☐ Grain ☐ Over/Under tolerance ☒ Cracks ☐ Broken/Damage/Defect ☐ Weld ☐ Part Incorrect ☐ Crimp/Kink/Ripple/Wave ☐ Inspection Incomplete/Unqualified ☐ Wrong Stock Pulled ☐ Part Lost/Missing ☐ Cuffs ☐ Contamination ☐ Out of Sequence ☐ Part Moved ☐ Crushing ☐ Countersink ☐ Off-set ☐ Drawing ☐ Heat Treat ☐ Cut Too Short ☐ Mislabeled ☐ Finish ☐ Wave/Twist in Tube ☐ Instructions Incomplete/Unclear ☐ Fit/Function ☐ Misread ☐ Marks/Chatter ☐ Drill Holes ☐ Misaligned/off center ☐ Turning Sequence ☐							
OTHER:									

Work Order ID 163662***163662***

Page 2

Wednesday, July 05, 2017 10:24:02 AM

Item ID: D350-748-201 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: Aft Crosstube AS350 / AS355
Start Date: 7/5/2017 Start Qty: 1.00 ***1*** Cust Item ID:
Required Date: 8/17/2017 Req'd Qty: 1.00 ***1*** Customer:
Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start ***NR1***
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
125	Outsource process - Heat Treat	0.00				1			DAS 13 9-30
125									
Outsource1	Memo	504.00							
Outsource process - Heat Treat	ISSUE P/O TO METCOR: 36962								
	Stress relief								
	Heat treat crosstube as per QSI010 4.3 within 12h after bending								
126	Receive & Inspect for Damage & Mat'l Certs	0.00							
126									
Packaging	Memo	0.02							
Packaging									
127	QC15- Crosstube Dimensional Check	0.00							
127									
QC	Memo	0.00							
Quality Control	***MARK CUT LINES***								

1x SQ17-7-10

JUL 13 2017

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
							Completed By		
							Lead hand / Supervisor Approval Verification		
							QC / QA Coordinator Approval		

Root Cause				FAULT CATEGORY			
Environment ☐	☐ No Re-verification	☐ Pressure/Forced	☐ Temperature/Cure	☐ Power Loss/Surge	☐ Positioned Wrong		
Design ☐	☐ Operator	☐ Bending	☐ Set-up	☐ Folio/Program	☐ Outside Dimensions		
Doc/Data ☐	☐ Offset/Setup	☐ Centre Not Concentric	☐ BOM/Route	☐ Grain	☐ Over/Under tolerance		
Equip/Tooling ☐	☐ Supplier	☐ Cracks	☐ Broken/Damage/Defect	☐ Weld	☐ Part Incorrect		
Handling/Pre ☐	☐ Training	☐ Crimp/Kink/Ripple/Wave	☐ Inspection Incomplete/Unqualified	☐ Wrong Stock Pulled	☐ Part Lost/Missing		
Material ☐	☐ Use for Testing	☐ Cuffs	☐ Contamination	☐ Out of Sequence	☐ Part Moved		
Internal Transport ☐	☐ Poor Information	☐ Crushing	☐ Countersink	☐ Off-set	☐ Drawing		
Tribal Knowledge ☐	☐ Rushing	☐ Heat Treat	☐ Cut Too Short	☐ Mislabeled	☐ Finish		
LOA ☐	☐ Product Improvement	☐ Wave/Twist in Tube	☐ Instructions Incomplete/Unclear	☐ Fit/Function	☐ Misread		
Substation ☐	☐ Process Improvement	☐ Marks/Chatter	☐ Drill Holes	☐ Misaligned/off center	☐ Turning Sequence		
Past Expiry Date ☐	☐ Manufacturing Process	OTHER : _____					
Misidentified ☐	☐ Past Due						

Work Order ID 163662***163662***

Page 3

Wednesday, July 05, 2017 10:24:02 AM

Item ID: D350-748-201

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Aft Crosstube AS350 / AS355

Start Date: 7/5/2017 Start Qty: 1.00

1

Cust Item ID:

Required Date: 8/17/2017 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals:

Process Plan: _____

Date: _____

Tooling: _____

Date: _____

Run Start ***NR1***

QC: _____

Date: _____

SPC (Y/N): _____

Date: _____

Stop ***NR2***Sequence ID/
Work Center IDOperation
DescriptionSet Up/
Run Hours

Tool ID

Tool #

Plan
CodeAccept
QtyReject
QtyReject
NumberInsp.
Stamp

128

0.00

128

Crosstubes

Memo

0.87

CUT TUBE AT HEIGHT ON FAI SHEET

VERF HEIGHT 31.6" BY QC 15 LEVEL INSPECTOR JWVERF TWIST 0.206 BY QC15 LEVEL INSPECTOR JWDPZ 17-07-13

130

2.09

130

Crosstubes

Crosstubes

Memo

0.48

2- Drill Tube as per Dwg D350-748-241 Using DT8876 Drill Jigs,
Set-up drill table as per QSI 010

3 -Deburr

4- Engrave Part # and Batch # as per Dwg D350-748-241

5-Remove all marks from tube within limits of D350-748-241

17-07-13JW
GP
DPZ17-07-13

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
								Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	

Root Cause			FAULT CATEGORY					
Environment ☐	☐ No Re-verification	☐ Pressure/Forced	☐ Temperature/Cure	☐ Power Loss/Surge	☐ Positioned Wrong			
Design ☐	☐ Operator	☐ Bending	☐ Set-up	☐ Folio/Program	☐ Outside Dimensions			
Doc/Data ☐	☐ Offset/Setup	☐ Centre Not Concentric	☐ BOM/Route	☐ Grain	☐ Over/Under tolerance			
Equip/Tooling ☐	☐ Supplier	☐ Cracks	☐ Broken/Damage/Defect	☐ Weld	☐ Part Incorrect			
Handling/Pre ☐	☐ Training	☐ Crimp/Kink/Ripple/Wave	☐ Inspection Incomplete/Unqualified	☐ Wrong Stock Pulled	☐ Part Lost/Missing			
Material ☐	☐ Use for Testing	☐ Cuffs	☐ Contamination	☐ Out of Sequence	☐ Part Moved			
Internal Transport ☐	☐ Poor Information	☐ Crushing	☐ Countersink	☐ Off-set	☐ Drawing			
Tribal Knowledge ☐	☐ Rushing	☐ Heat Treat	☐ Cut Too Short	☐ Mislabeled	☐ Finish			
LOA ☐	☐ Product Improvement	☐ Wave/Twist in Tube	☐ Instructions Incomplete/Unclear	☐ Fit/Function	☐ Misread			
Substation ☐	☐ Process Improvement	☐ Marks/Chatter	☐ Drill Holes	☐ Misaligned/off center	☐ Turning Sequence			
Past Expiry Date ☐	☐ Manufacturing Process	OTHER : _____						
Misidentified ☐	☐ Past Due							

Work Order ID 163662***163662***

Page 4

Wednesday, July 05, 2017 10:24:02 AM

Item ID: D350-748-201

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Aft Crosstube AS350 / AS355

Start Date: 7/5/2017 Start Qty: 1.00 ***1***

Cust Item ID:

Required Date: 8/17/2017 Req'd Qty: 1.00 ***1***

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start ***NR1***

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

140

QC6- All purchased or subcontracted products

0.00

140

QC

Memo

0.00

Quality Control

JUL 14 2017

150

Outsource process-Cadplate per QSI017 4.1.9.1

0.00

150

Outsource3

Memo

360.00

Outsource process - Cad plate

Issue P/O: 37045
Stress relief at 375° for 5 hours
Magnetic Particle Inspect per ASTM E1444
Cadium Plate per AMS-QQ-P-416B, Class 1, Type 2
Embrittle relief at 375° for 8 hours, Chromate Treat
Possible Supplier: Southwest United Industries
Ensure Certificate of Conformity is attached

DAS
13
9-89

11/17/17/24

160

Receive & Inspect for Damage & Mat'l Certs

0.00

160

Packaging

Memo

0.02

Packaging

Ensure certificate of conformity is attached

1X SP17-7-25

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval 	
Description Work Order Deviation				Disposition					
								Completed By 	
								Lead hand / Supervisor Approval Verification 	
								QC / QA Coordinator Approval 	

Root Cause			FAULT CATEGORY							
Environment	☐	No Re-verification	☐	Pressure/Forced	☐	Temperature/Cure	☐	Power Loss/Surge	☐	Positioned Wrong
Design	☐	Operator	☐	Bending	☐	Set-up	☐	Folio/Program	☐	Outside Dimensions
Doc/Data	☐	Offset/Setup	☐	Centre Not Concentric	☐	BOM/Route	☐	Grain	☐	Over/Under tolerance
Equip/Tooling	☐	Supplier	☐	Cracks	☐	Broken/Damage/Defect	☐	Weld	☐	Part Incorrect
Handling/Pre	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐	Inspection Incomplete/Unqualified	☐	Wrong Stock Pulled	☐	Part Lost/Missing
Material	☐	Use for Testing	☐	Cuffs	☐	Contamination	☐	Out of Sequence	☐	Part Moved
Internal Transport	☐	Poor Information	☐	Crushing	☐	Countersink	☐	Off-set	☐	Drawing
Tribal Knowledge	☐	Rushing	☐	Heat Treat	☐	Cut Too Short	☐	Mislabeled	☐	Finish
LOA	☐	Product Improvement	☐	Wave/Twist in Tube	☐	Instructions Incomplete/Unclear	☐	Fit/Function	☐	Misread
Substation	☐	Process Improvement	☐	Marks/Chatter	☐	Drill Holes	☐	Misaligned/off center	☐	Turning Sequence
Past Expiry Date	☐	Manufacturing Process	☐	OTHER :						
Misidentified	☐	Past Due	☐							

Work Order ID 163662***163662***

Page 5

Wednesday, July 05, 2017 10:24:02 AM

Item ID: D350-748-201

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Aft Crosstube AS350 / AS355

Start Date: 7/5/2017 Start Qty: 1.00

1

Cust Item ID:

Required Date: 8/17/2017 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals:

Process Plan: _____

Date: _____

Tooling: _____

Date: _____

Run Start ***NR1***

QC: _____

Date: _____

SPC (Y/N): _____

Date: _____

Stop ***NR2***Sequence ID/
Work Center IDOperation
DescriptionSet Up/
Run Hours

Tool ID

Tool #

Plan
CodeAccept
QtyReject
QtyReject
NumberInsp.
Stamp

170

QC6- All purchased or subcontracted products

0.00

170

QC

Memo

0.02

Quality Control

DAS
38
9-89

JUL 25 2017

174

Outsource process - NDT per QSI038 4.1

0.00

174

Outsource2

Memo

48.00

Outsource process - NDT

ISSUE P/O TO ACCUREN: 3711

JUL 2017/07/25

176

Receive & Inspect for Damage & Mat'l Certs

0.00

176

Packaging

Memo

0.02

Packaging

1 17-07-25

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval Completed By _____ Lead hand / Supervisor Approval Verification _____ QC / QA Coordinator Approval _____	
Description Work Order Deviation				Disposition					
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐							
		OTHER : ☐							

Work Order ID 163662***163662***

Page 6

Wednesday, July 05, 2017 10:24:02 AM

Item ID: D350-748-201

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Aft Crosstube AS350 / AS355

Start Date: 7/5/2017 Start Qty: 1.00 ***1***

Cust Item ID:

Required Date: 8/17/2017 Req'd Qty: 1.00 ***1***

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start ***NR1***

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

178

QC5- Inspect part completeness to step on W/O

0.00

178

QC

Memo

0.02

Quality Control

JB
17-07-25

180

Spray Painting per QSI005 4.2

0.00

180

SprayPaint

SprayPaint

Memo

1.50

Spray Painting

***VERIFY BY _____ BATCH # TO MATCH W/O

163662

***VERIFY BY _____ PART # TO MATCH

W/O 163662

MASK SCRIBE B# & P# AND VERIFY

1-Prime inside and out crosstube as per QSI 005 4.2

BATCH: 137487

2-Paint Outside of Tube as per Dart QSI 005 4.2

BATCH: 137852

DAS
41
9-89

JUL 26 2017

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
				Completed By 					
				Lead hand / Supervisor Approval Verification 					
				QC / QA Coordinator Approval 					

Root Cause			FAULT CATEGORY							
Environment ☐	☐	No Re-verification	☐	Pressure/Forced	☐	Temperature/Cure	☐	Power Loss/Surge	☐	Positioned Wrong
Design ☐	☐	Operator	☐	Bending	☐	Set-up	☐	Folio/Program	☐	Outside Dimensions
Doc/Data ☐	☐	Offset/Setup	☐	Centre Not Concentric	☐	BOM/Route	☐	Grain	☐	Over/Under tolerance
Equip/Tooling ☐	☐	Supplier	☐	Cracks	☐	Broken/Damage/Defect	☐	Weld	☐	Part Incorrect
Handling/Pre ☐	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐	Inspection Incomplete/Unqualified	☐	Wrong Stock Pulled	☐	Part Lost/Missing
Material ☐	☐	Use for Testing	☐	Cuffs	☐	Contamination	☐	Out of Sequence	☐	Part Moved
Internal Transport ☐	☐	Poor Information	☐	Crushing	☐	Countersink	☐	Off-set	☐	Drawing
Tribal Knowledge ☐	☐	Rushing	☐	Heat Treat	☐	Cut Too Short	☐	Mislabeled	☐	Finish
LOA ☐	☐	Product Improvement	☐	Wave/Twist in Tube	☐	Instructions Incomplete/Unclear	☐	Fit/Function	☐	Misread
Substation ☐	☐	Process Improvement	☐	Marks/Chatter	☐	Drill Holes	☐	Misaligned/off center	☐	Turning Sequence
Past Expiry Date ☐	☐	Manufacturing Process	OTHER : _____							
Misidentified ☐	☐	Past Due								

Work Order ID 163662***163662***

Page 7

Wednesday, July 05, 2017 10:24:02 AM

Item ID: D350-748-201

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Aft Crosstube AS350 / AS355

Start Date: 7/5/2017 Start Qty: 1.00

1

Cust Item ID:

Required Date: 8/17/2017 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start ***NR1***

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***Sequence ID/
Work Center IDOperation
DescriptionSet Up/
Run Hours

Tool ID

Tool #

Plan
CodeAccept
QtyReject
QtyReject
NumberInsp.
Stamp

190

QC14- Inspect Spray Paint

0.00

190

QC

Quality Control

Memo

0.01

Then, Wrap in plastic bag to protect from scratches

VERIFY BY JB BATCH # TO MATCH W/OVERIFY BY JB PART # TO MATCHW/O 1636621 JB
17-07-31

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval Completed By _____ Lead hand / Supervisor Approval Verification _____ QC / QA Coordinator Approval _____	
Description Work Order Deviation				Disposition					
Root Cause		FAULT CATEGORY							
Environment ☐	☐ No Re-verification	☐ Pressure/Forced	☐ Temperature/Cure	☐ Power Loss/Surge	☐ Positioned Wrong				
Design ☐	☐ Operator	☐ Bending	☐ Set-up	☐ Folio/Program	☐ Outside Dimensions				
Doc/Data ☐	☐ Offset/Setup	☐ Centre Not Concentric	☐ BOM/Route	☐ Grain	☐ Over/Under tolerance				
Equip/Tooling ☐	☐ Supplier	☐ Cracks	☐ Broken/Damage/Defect	☐ Weld	☐ Part Incorrect				
Handling/Pre ☐	☐ Training	☐ Crimp/Kink/Ripple/Wave	☐ Inspection Incomplete/Unqualified	☐ Wrong Stock Pulled	☐ Part Lost/Missing				
Material ☐	☐ Use for Testing	☐ Cuffs	☐ Contamination	☐ Out of Sequence	☐ Part Moved				
Internal Transport ☐	☐ Poor Information	☐ Crushing	☐ Countersink	☐ Off-set	☐ Drawing				
Tribal Knowledge ☐	☐ Rushing	☐ Heat Treat	☐ Cut Too Short	☐ Misabeled	☐ Finish				
LOA ☐	☐ Product Improvement	☐ Wave/Twist in Tube	☐ Instructions Incomplete/Unclear	☐ Fit/Function	☐ Misread				
Substation ☐	☐ Process Improvement	☐ Marks/Chatter	☐ Drill Holes	☐ Misaligned/off center	☐ Turning Sequence				
Past Expiry Date ☐	☐ Manufacturing Process	OTHER : _____							
Misidentified ☐	☐ Past Due								

Work Order ID 163662***163662***

Page 8

Wednesday, July 05, 2017 10:24:02 AM

Item ID: D350-748-201

Accept

N900040100

Setup Start

NS1

Revision ID:

Stop

NS2

Item Name: Aft Crosstube AS350 / AS355

Start Date: 7/5/2017 Start Qty: 1.00

1

Cust Item ID:

Required Date: 8/17/2017 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals:

Process Plan: _____

Date: _____

Tooling: _____

Date: _____

Run Start

NR1

QC: _____

Date: _____

SPC (Y/N): _____

Date: _____

Stop

NR2Sequence ID/
Work Center IDOperation
DescriptionSet Up/
Run Hours

Tool ID

Tool #

Plan
CodeAccept
QtyReject
QtyReject
NumberInsp.
Stamp

200

0.00

200

Crosstubes

Crosstubes

Memo

2.77

INSTALL GROUND WIRE INSERT, THEN INSERT SCREW AND WASHER

1-Abrade mating surfaces of support and crosstube with 180 grit sandpaper,
clean the area with MEK or equivalent as per dwg

2-Install supports with Proseal 890 per D350-748-241 and QSI 015

A/R Proseal 890

Batch: 137495EXP: 1/183-Install supports clamps Using Dt8876 as per Dwg D350-748-241, Torque to
60-80 IN-LBS.

PROSEAL CURE TIME 72 HOURS:

Start: 17-7-27Finish: 17-7-30

DAS

41

9-89

JUL 27 2017

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐	OTHER : _____							
Misidentified ☐	Past Due ☐								

Work Order ID 163662***163662***

Page 9

Wednesday, July 05, 2017 10:24:02 AM

Item ID: D350-748-201

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Aft Crosstube AS350 / AS355

Start Date: 7/5/2017 Start Qty: 1.00 ***1***

Cust Item ID:

Required Date: 8/17/2017 Req'd Qty: 1.00 ***1***

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start ***NR1***

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

210

QC5- Inspect part completeness to step on W/O

0.00

210

QC

Quality Control

Memo

0.02

***RE-CHECK TORCQUE ON CLAMP AFTER PROSEAL HAS CURED
FOR 72HOURS AS PER DWG.******VERIFY BY 163662 BATCH # TO MATCH W/O***VERIFY BY 163662 PART # TO MATCHW/O 1636621
JB
17-07-31

220

Pick Kit

0.00

220

Packaging

Packaging

Memo

0.00

JUL 27 2017

DAS
6
9-89DAS
26
9-89

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐							
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval			
Description Work Order Deviation				Disposition				Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval			
Root Cause		FAULT CATEGORY									
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐	Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐	Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐	Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐	Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐	Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐
Past Expiry Date ☐	Manufacturing Process ☐	OTHER : ☐									
Misidentified ☐	Past Due ☐										

Work Order ID 163662

Wednesday, July 05, 2017 10:24:02 AM

163662

Page 10

Item ID: D350-748-201

Accept

N900040100

Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Aft Crosstube AS350 / AS355

Start Date: 7/5/2017 Start Qty: 1.00 ***1***

Cust Item ID:

Required Date: 8/17/2017 Req'd Qty: 1.00 ***1***

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start ***NR1***

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
230 *230* QC Quality Control	QC4- 100% Inspect kits for completeness Memo ***VERIFY BY <u>163662</u> BATCH # TO MATCH W/O ***VERIFY BY <u>163662</u> PART # TO MATCH W/O <u>163662</u>	0.00 0.03							
						DAS 28 9-89		JUL 3 1 2017	
240 *240* Packaging Packaging	Identify as per dwg & Stock Location: <u>163662</u> Packaging Memo Identify and pack for shipping as per PPPD350-748-201 Location: FG035	0.00 0.00							
						DAS 28 9-89		JUL 3 1 2017	
250 *250* QC Quality Control	QC21- Final Inspection - Work Order Release Memo	0.00 0.10							
						DAS 21 9-89		JUL 3 1 2017	

DAS
21
9-89
JUL 3 1 2017

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
							Completed By		
							Lead hand / Supervisor Approval Verification		
							QC / QA Coordinator Approval		

Root Cause			FAULT CATEGORY					
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐			
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐			
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐			
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐			
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐			
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐			
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐			
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐			
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐			
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐			
Past Expiry Date ☐	Manufacturing Process ☐	OTHER : ☐						
Misidentified ☐	Past Due ☐							

Picklist Print

Wednesday, July 05, 2017 10:24:05 AM

Page 1

Work Order ID: 163662

163662

Parent Item: D350-748-201

D350-748-201

Parent Item Name: Aft Crosstube AS350 / AS355

Start Date: 7/5/2017

Required Date: 8/17/2017

Start Qty: 1.00

Required Qty: 1.00

Comments: IPP Rev: A New Issue 06-07-05 JLM
 IPP Rev: B Update qty of MS21042L5 06-09-12 KJ
 IPP Rev C Combined manufacturing 08.04.02 EC verified by: DD
 IPP Rev:D 08-06-24 revD as per dwg DD verified by:EC
 IPP Rev: E 08.12.11 Step17 was step 21 KJ Verified by:EC IPP Rev:F
 10.08.04 added QSI010 4.3 DD verf:EC IPP REV:G ADD
 UNDER BEND COMMENT 12-05-28 JLM IPP REV:H 12.11.05 as per
 dwg D350-748-141G DD verf:JLM IPP REV:I 15.03.19 as per dwg D350-748-
 241revH dd verf:jlm

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
---------------------------------	------------------------	---------------	-------------	---------------------	------------------	-----------------	--------------------	----------------	-------------	--------------	---------------	----------------	--------

D350-748-241TRN

Manufactured

No

110

Each

12.0000

1

1

D350-748-241TRN

**

Crosstube Turning Detail

D12 17-07-07

Location	Loc Qty	Loc Code
HALL	12	
158702	1	
158703	1	
158704	1	
158705	1	
158706	1	
158707	1	
158708	1	
158709	1	
158721	1	
158722	1	
158723	1	
158725	1	

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐								
Misidentified ☐	Past Due ☐	OTHER : ☐							

Picklist Print

Wednesday, July 05, 2017 10:24:05 AM

Page 2

Work Order ID: 163662

163662

Parent Item: D350-748-201

D350-748-201

Parent Item Name: Aft Crosstube AS350 / AS355

Start Date: 7/5/2017

Required Date: 8/17/2017

Start Qty: 1.00

Required Qty: 1.00

ALS4-1032-225 AEELS8-1032-225 Purchased

No

200

Each

2,620.000

1

1

ALS4-1032-225

Rivnut

**

DAS
41
9-89

JUL 30 2017

Location

Loc Qty

Loc Code

FG

55

M134975

20

M135998

5

M136579

30

FP001

2200

M135603

40

M135920

38

M135998

2111

M136265

11

ST556

365

M136579

365

1

MS21920-20

Purchased

No

200

Each

146.0000

2

2

MS21920-20

Clamp

**

DAS
41
9-89

JUL 30 2017

Location

Loc Qty

Loc Code

FG

2

122254

2

LG050

142

m137361

17

m137587

50

m137710

50

m137820

25

2

LG056

2

m128650

1

m132675

1

Wednesday, July 05, 2017 10:24:05 AM

Shop Packet Print

Page 2

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐				
OTHER : ☐									

Picklist Print

Wednesday, July 05, 2017 10:24:05 AM

Page 3

Work Order ID: 163662

163662

Parent Item: D350-748-201

D350-748-201

Parent Item Name: Aft Crosstube AS350 / AS355

Start Date: 7/5/2017

Required Date: 8/17/2017

Start Qty: 1.00

Required Qty: 1.00

MS27039-1-10

Purchased

No

200

Each

170.0000

1

1

DAS

41

9-89

JUL 30 2017

MS27039-1-10

SCREW

**

Location

Loc Qty

Loc Code

GA

15

m129541

15

over006

119

m137736

119

ST280

36

m137164

6

m137597

30

D5123-7

Manufactured

No

200

Each

104.0000

2

2

DAS

41

9-89

JUL 30 2017

D5123-7

Clamp Cushion

**

Location

Loc Qty

Loc Code

LG052

104

151551

12

153236

92

D3502-1

Manufactured

No

200

Each

58.0000

2

2

DAS

41

9-89

JUL 30 2017

D3502-1

Support

**

Location

Loc Qty

Loc Code

LG052

58

150010

14

150683

2

158881

20

161764

22

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval Completed By _____ Lead hand / Supervisor Approval Verification _____ QC / QA Coordinator Approval _____	
Description Work Order Deviation				Disposition					

Root Cause			FAULT CATEGORY							
Environment ☐	☐	No Re-verification	☐	Pressure/Forced	☐	Temperature/Cure	☐	Power Loss/Surge	☐	Positioned Wrong
Design ☐	☐	Operator	☐	Bending	☐	Set-up	☐	Folio/Program	☐	Outside Dimensions
Doc/Data ☐	☐	Offset/Setup	☐	Centre Not Concentric	☐	BOM/Route	☐	Grain	☐	Over/Under tolerance
Equip/Tooling ☐	☐	Supplier	☐	Cracks	☐	Broken/Damage/Defect	☐	Weld	☐	Part Incorrect
Handling/Pre ☐	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐	Inspection Incomplete/Unqualified	☐	Wrong Stock Pulled	☐	Part Lost/Missing
Material ☐	☐	Use for Testing	☐	Cuffs	☐	Contamination	☐	Out of Sequence	☐	Part Moved
Internal Transport ☐	☐	Poor Information	☐	Crushing	☐	Countersink	☐	Off-set	☐	Drawing
Tribal Knowledge ☐	☐	Rushing	☐	Heat Treat	☐	Cut Too Short	☐	Mislabeled	☐	Finish
LOA ☐	☐	Product Improvement	☐	Wave/Twist in Tube	☐	Instructions Incomplete/Unclear	☐	Fit/Function	☐	Misread
Substation ☐	☐	Process Improvement	☐	Marks/Chatter	☐	Drill Holes	☐	Misaligned/off center	☐	Turning Sequence
Past Expiry Date ☐	☐	Manufacturing Process	OTHER : _____							
Misidentified ☐	☐	Past Due								

Picklist Print

Wednesday, July 05, 2017 10:24:05 AM

Page 4

Work Order ID: 163662

163662

Parent Item: D350-748-201

D350-748-201

Parent Item Name: Aft Crosstube AS350 / AS355

Start Date: 7/5/2017

Required Date: 8/17/2017

Start Qty: 1.00

Required Qty: 1.00

NAS1149D0363J

Purchased

No

200

Each

631.0000

1

1

NAS1149D0363J

Washer

**

DAS
41
9-89

JUL 30 2017

Location

Loc Qty

Loc Code

GA

43

m134055

13

m137164

30

ST263

588

m137587

588

AN4-6A

Purchased

No

220

Each

551.0000

16

16

AN4-6A

BOLT

**

Location

Loc Qty

Loc Code

ST345

551

M137464

551

AN5-32A

Purchased

No

220

Each

243.0000

4

4

AN5-32A

Bolt

**

Location

Loc Qty

Loc Code

over004

120

m137853

120

ST336

123

m137320

3

m137464

120

D3500-1

Manufactured

No

220

Each

40.0000

4

4

D3500-1

Saddle

**

Location

Loc Qty

Loc Code

ST406

40

158741

40

Wednesday, July 05, 2017 10:24:05 AM

Shop Packet Print

Page 4

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By _____ Lead hand / Supervisor Approval Verification _____ QC / QA Coordinator Approval _____		
Description Work Order Deviation				Disposition					
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐	OTHER : _____							
Misidentified ☐	Past Due ☐								

Picklist Print

Wednesday, July 05, 2017 10:24:05 AM

Page 5

Work Order ID: 163662

163662

Parent Item: D350-748-201

D350-748-201

Parent Item Name: Aft Crosstube AS350 / AS355

Start Date: 7/5/2017

Required Date: 8/17/2017

Start Qty: 1.00

Required Qty: 1.00

NAS1149D0463J

Purchased

No

220

Each

3,313.000

32

32

NAS1149D0463.J

Washer

**

JUL 27 2017

DAS
6
9-89

DAS
28
9-89

Location

Loc Qty

Loc Code

GA

40

M135056

40

ST260a

2000

M137699

2000

ST263

1273

M137371

1273

220

Each

240.0000

8

8

AN4-41A

Purchased

No

AN4-41A

Bolt

**

JUL 27 2017

DAS
6
9-89

DAS
26
9-89

DAS
28
9-89

Location

Loc Qty

Loc Code

over003

161

m137464

41

m137544

120

ST342

79

m133769

2

m136851

37

m137320

40

220

Each

379.0000

16

16 JUL 27 2017

**

D3501-1

Manufactured

No

D3501-1

Bushing

Location

Loc Qty

Loc Code

ST037

61

159311

61

ST038A

318

152871

0

161783

120

162915

198

DAS
28
9-89

DAS
6
9-89

DAS
26
9-89

Wednesday, July 05, 2017 10:24:05 AM

Shop Packet Print

Page 5

DQA: _____ Date: _____

WORK ORDER NON-CONFORMANCE / UPDATE



QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date : _____		Step #: _____		QTY Effective : _____			MRB (QSI042) Approval Completed By _____ Lead hand / Supervisor Approval Verification _____ QC / QA Coordinator Approval _____		
Description Work Order Deviation				Disposition					
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐							
		☐ OTHER : _____							

Picklist Print

Wednesday, July 05, 2017 10:24:05 AM

Page 6

Work Order ID: 163662

163662

Parent Item: D350-748-201

D350-748-201

Parent Item Name: Aft Crosstube AS350 / AS355

Start Date: 7/5/2017

Required Date: 8/17/2017

Start Qty: 1.00

Required Qty: 1.00

MS21042L4

Purchased

No

220

Each

1,899.000

24

24

MS21042L4

Nut

**

DAS

6
9-89

JUL 27 2017

DAS
26
9-89

Location

Loc Qty

Loc Code

FP001

10

m133363

10

GA

51

m135058

51

OVER007

1000

m137680

1000

ST303

838

m137402

400

m137544

438

24

NAS1149D0563J

Purchased

No

220

Each

1,548.000

8

8

NAS1149D0563J

Washer

**

DAS

6
9-89

JUL 27 2017

DAS
26
9-89

Location

Loc Qty

Loc Code

GA

36

m135774

36

ST260a

700

m137820

700

ST263

812

m137587

812

8

DAS
28
9-89

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date : _____		Step #: _____		QTY Effective : _____			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
				Completed By _____					
				Lead hand / Supervisor Approval Verification _____					
				QC / QA Coordinator Approval _____					
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐	OTHER : _____							
Misidentified ☐	Past Due ☐								

Picklist Print

Wednesday, July 05, 2017 10:24:05 AM

Page 7

Work Order ID: 163662

163662

Parent Item: D350-748-201

D350-748-201

Parent Item Name: Aft Crosstube AS350 / AS355

Start Date: 7/5/2017

Required Date: 8/17/2017

Start Qty: 1.00

Required Qty: 1.00

MS21042L5

Purchased

No

220

Each

565.0000

4

4

MS21042L5

**

JUL 27 2017

Nut

Location

Loc Qty

Loc Code

GA

12

m127813

12

ST303

553

m137478

53

m137587

500

DAS
28
9-89

DAS
6
9-89

DAS
26
9-89

Wednesday, July 05, 2017 10:24:05 AM

Shop Packet Print

Page 7

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____


Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date : _____		Step #: _____		QTY Effective : _____			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
							Completed By		
							Lead hand / Supervisor Approval Verification		
							QC / QA Coordinator Approval		
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐							
OTHER : ☐									

Before De-stress

DART AEROSPACE LTD		Work Order:	163662
Description: Crosstube High Aft (AS350/355)		Part Number:	D350-748-201
Inspection Dwg: D350-748-241 Rev: H		Page 1 of 1	

Required Dimension	Min	Max
Height	31.10	31.60
1/2 Span	40.77	41.03
Angle	75	77
Total Span	81.54	82.06
Bending Passes	7	--
Crushing	--	8%
Twist	--	0.38

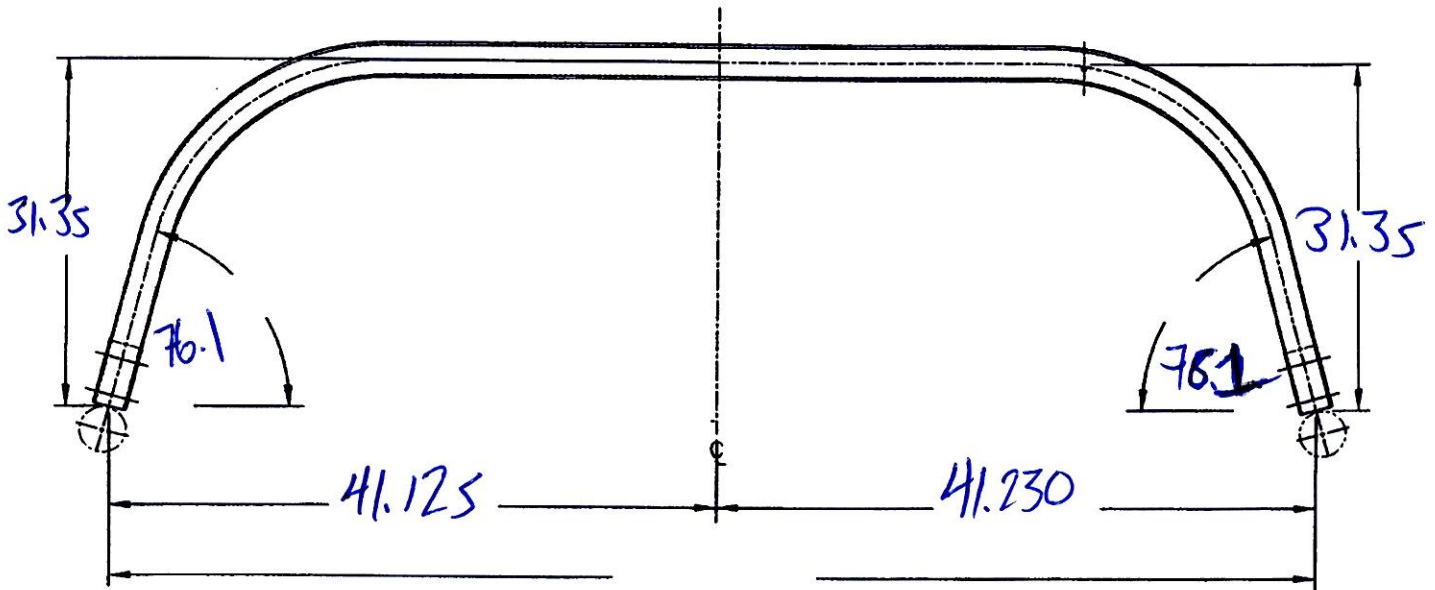

	Side A	Side B
Bending Passes	42	41
Crushing		
Comments		

QC15 Inspection	
Date	

Rev	Date	Change	Revised by	Approved
A	07.02.06	New Issue	KJ/JM	
B	10.08.23	Dwg Rev updated	KJ	
C	12.04.16	Added bending, crushing & twist dimensions	KJ	
D	12.07.31	Dwg Rev updated	KJ	
E	13.02.27	Dwg Rev updated	KJ	
F	14.02.13	Crushing & twist dimensions revised	KJ	
G	14.11.10	Height dimension revised	KJ	
H	15.07.20	Crushing dimension revised	KJ	

Item	Qty	Part Number	Description
	-241		
1	X	D350-748-241	CROSSTUBE ASSEMBLY (AS 350/355 HI AFT)
2	1	D6015-125	CROSSTUBE (OR D6018-125)
3	2	D3502-1	SUPPORT
4	2	D5123-7	CLAMP CUSHION
5	1	AELS-1032-225	INSERT
6	1	NAS1149D0363J	WASHER (OR AN960JD10)
7	2	MS21920-20	CLAMP (OR MS21920-21/-22, PER DART SPEC. M-MS21920-21/-22)
8	1	MS27039-1-10	SCREW
9	A/R	PROSEAL 890 B-2	SEALANT, AMS-S-8802 CLASS B-2

GENERAL NOTES:

- MATERIAL: MANUFACTURED FROM D6015-125 OR D6018-125
FINISHED LENGTH AFTER TURNING = 124.70±0.06 (AFTER BENDING/TRIMMING = 122.70 REF)
- FINISH: MAGNETIC PARTICLE INSPECT PER DART QSI 038 4.2
CADMIUM PLATE PER AMS-QQ-P-416B, CLASS 1, TYPE II
PRIME INSIDE AND OUTSIDE PER DART QSI 005 4.2
PAINT OUTSIDE PER DART QSI 005 4.2
- TOLERANCE: PER DART QSI 018 UNLESS OTHERWISE NOTED.
WALL THICKNESS ECCENTRICITY PER DART QSI 038 7.2
MIN. ALLOWABLE WALL IS -0.020 FROM NOMINAL
- UNITS: INCHES UNLESS OTHERWISE NOTED.
- BREAK SHARP EDGES: 0.005 TO 0.010 MAX.
- IDENTIFICATION: DART PART NUMBER "D350-748-241" AND BATCH NUMBER ON INSIDE OF CUFF
PER DART QSI 044 6.4 (VIBRATING STYLUS)
- WEIGHT: 29.85 lbs
- PART IS SYMMETRIC ABOUT CENTERLINE, EXCEPT FOR Ø0.297 HOLE.
- EXTREME CARE MUST BE TAKEN TO PROTECT THE OUTSIDE SURFACE OF THE TUBE. THE OUTSIDE SURFACE MUST BE SMOOTH AND FREE FROM SURFACE DEFECTS SUCH AS SCRATCHES, NICKS, OR DENTS. DEFECTS UP TO 0.005" MAY BE BLENDED OUT LONGITUDINALLY. CIRCUMFERENTIAL GRIND MARKS ARE UNACCEPTABLE. WHEN DRILLING HOLES EXTREME CARE MUST BE TAKEN AND CAREFUL DEBURRING PERFORMED TO ENSURE A CLEAN HOLE WITH NO CRACKING/CHIPPING/GROOVES.

TURNING

- BLEND OUT ALL EDGES FROM MACHINING LONGITUDINALLY, TRANSITION SHOULD BE SMOOTH. NOTE: ALL HOLES ARE DRILLED AFTER BENDING.
- HEAT TREAT TO MIN. 180 KSI PER MIL-T-6736 OR AMS2759/1E AFTER TURNING. ACCEPTABLE TO VERIFY TENSILE STRENGTH BY HARDNESS TEST PER ASTM E18 TO 40-45 HRC.

BENDING

- ALL DIMENSIONS FOR BENT TUBE ARE POST STRESS RELIEF
- BEND PROGRESSIVELY WITH A MINIMUM OF 7 PASSES PER SIDE. MAXIMUM TUBE FLATTENING DUE TO BENDING IS 8% BASED ON O.D. ON TOP HALF OF BEND, AND 8% ON BOTTOM HALF OF BEND.
- MAX AMPLITUDE OF RIPPING ALONG BENT PORTION OF THE TUBE IS 0.030 (ZIN A1-3)
- AFTER BENDING, STRESS RELIEVE TUBE AT 650°F ±10.25°F FOR A MINIMUM OF 2 HRS AND ALLOW TO COOL TO AMBIENT TEMPERATURE (REF AMS2759/1E).
- MAX TWIST AFTER STRESS RELIEF: WITH XTUBE LAYED FLAT ON SURFACE, THE DIFFERENCE BETWEEN CUFF HEIGHTS FROM THE SURFACE MAY BE NO LARGER THAN 0.38 (ZIN C1-3).

ASSEMBLY

- TO INSTALL D3502-1 SUPPORT: ABRASE MATING SURFACE OF SUPPORT AND CROSSTUBE WITH 180-GRIT SANDPAPER AND REMOVE RESIDUE WITH MEK (OR EQUIVALENT). APPLY A 0.02" TO 0.05" THICK LAYER OF PROSEAL 890 CLASS B-2 (OR AMS-S-8802 CLASS B-2) SEALANT TO MATING SURFACE OF SUPPORT.
- TORQUE CLAMPS 60 TO 80 IN-LB. ENSURE AT LEAST 1.5 THREADS SHOWING IN SAFETY AND THAT NUT HAS NOT BOTTOMED-OUT AFTER TORQUING. PRIOR TO PACKAGING, RE-CHECK TORQUE ON CLAMPS AFTER PROSEAL 890 SEALANT HAS CURED FOR 72 HOURS.

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER

NO. 163662 M15
1707-05

RELEASED

2015 MAR 18

97 ECU 15-547

H	D5123-7 WAS D3595-063-395, MS21920-20 WAS -22, ALLOWABLE CRUSHING NOW 8% WAS 7%, 14.00 WAS 14.37 (D5-2), 12.32 WAS 12.89 (D5-3)	CP	15.02.25
G	RMV ABRASION STRIP, SUPPORT NOW W/ PROSEAL & CUSHION, ADD STRESS RELIEF, LONGER CUFF, NOW TRIM'D AFTER BEND, ADD WALL DIMS & UPDATE TOL.	CP	12.09.12
F	ADD HRC TEST OPTION (B8-1) PER PAR 09-040, ADD TWIST LIMIT (A8-1, C1-3), ADD D6015-125 OPTION (C8-1), STOCK DIM NOW MACHINED (D1-4)	CP	10.11.23
E	REVISE GENERAL NOTES; UPDATE TO CURRENT STANDARDS; RELOCATED FLAG #6 PER PAR 08-046 (ZIN A8-3); ADD TOLERANCES (ZIN C8-3, D2-3)	RF	09.09.30
D	MAG. PARTICLE AND CAD PLATE AS MFD.	CP	08.10.31
C	ADD CAD PLATING	CP	06.08.14
B	ADD D6018-125 & PRIME AND PAINT	CP	06.08.30
A	NEW ISSUE	CP	06.03.31
REV.	DESCRIPTION	BY	DATE
DESIGN			
DRAWN			
CHECKED			
MFG. APPR.			
APPROVED			
DE APPR.			
DATE	15.02.25		

DART AEROSPACE LTD
HAWKESBURY, ONTARIO, CANADA

DRAWING NO.
D350-748-241

REV. H
SHEET 1 OF 4

TITLE
CROSSTUBE (AS 350/355 HI AFT)

SCALE
NTS

COPYRIGHT © 2008 BY DART AEROSPACE LTD
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR DISCLOSED OR REPRODUCED IN ANY MANNER WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

DQA: _____ Date: _____




WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐				
OTHER : ☐									

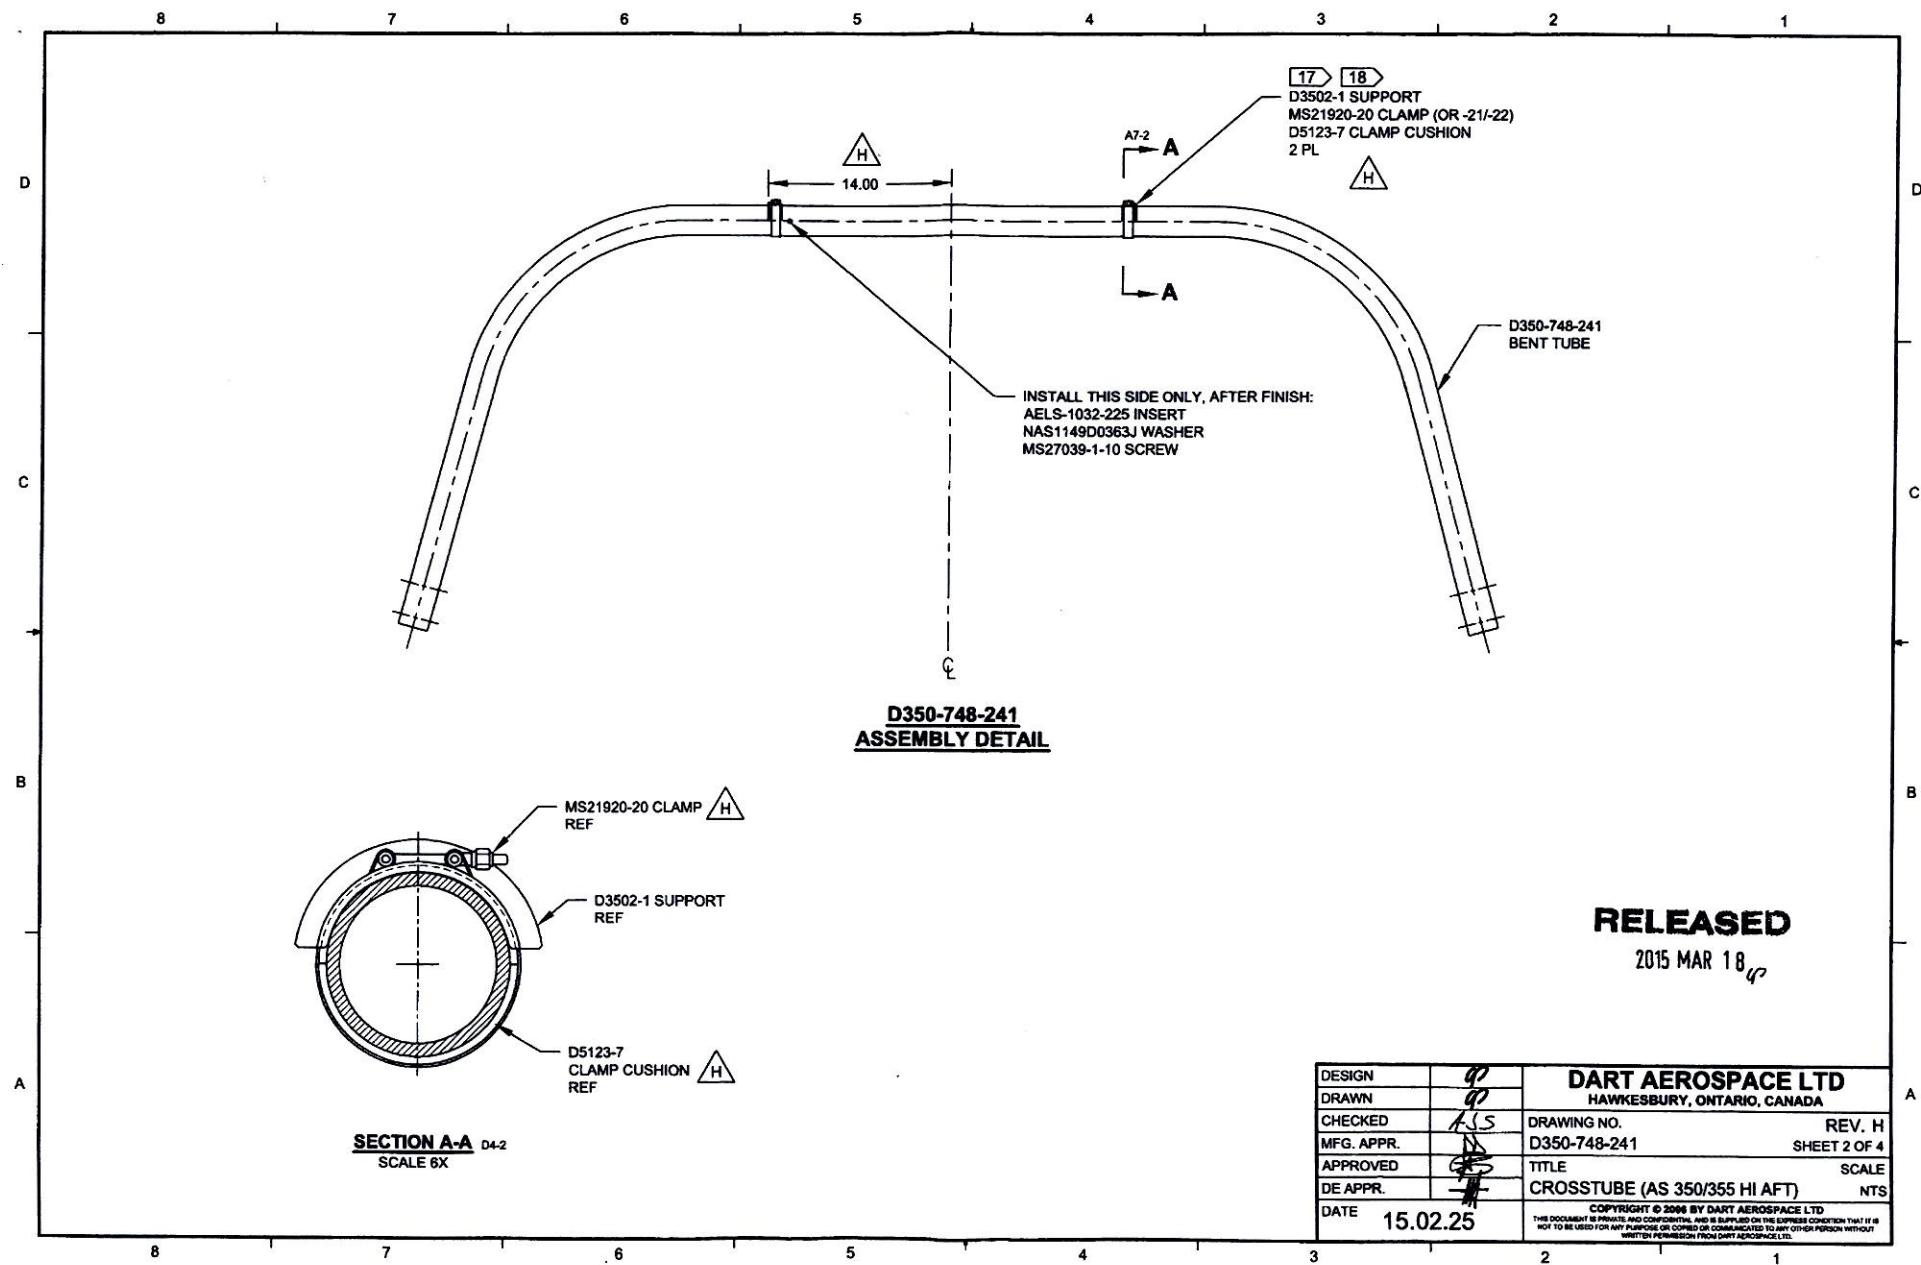

DQA: _____ Date: _____




WORK ORDER NON-CONFORMANCE / UPDATE


QA Closed: _____ Date: _____

Work Order update only ☐


Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐								
Misidentified ☐	Past Due ☐	OTHER : ☐							

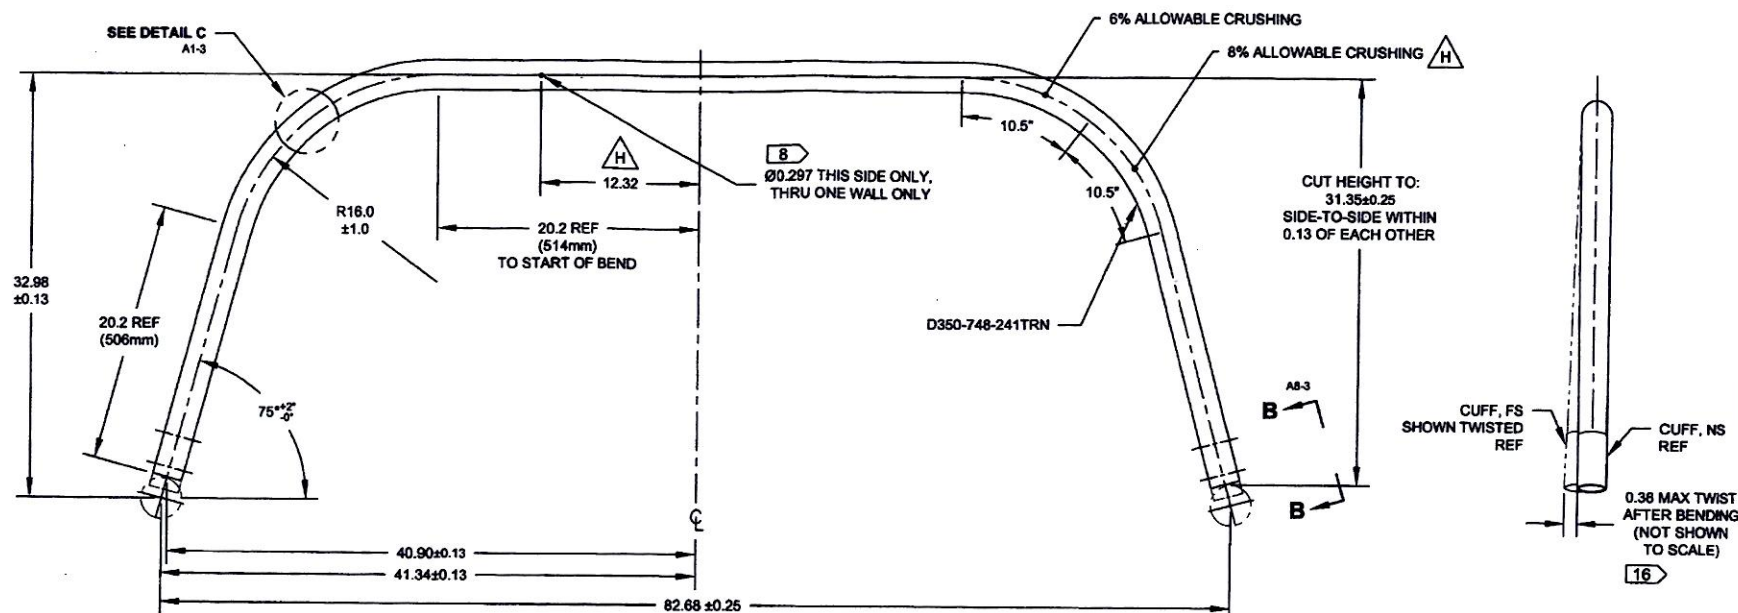

**D350-748-241
BENDING AND DRILLING DETAIL 10**

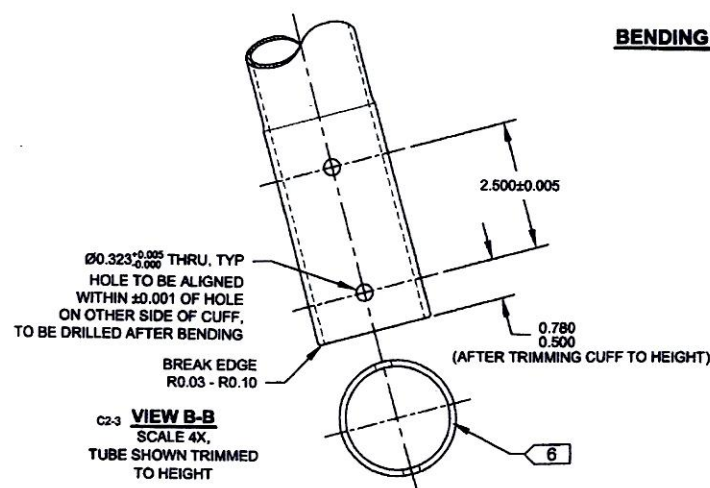

VIEW B-B
SCALE 4X,
TUBE SHOWN TRIMMED
TO HEIGHT

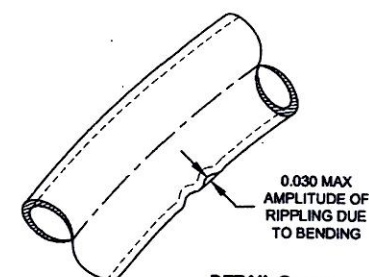

DETAIL C D7-3
SCALE 4X
RIPPING EXAGGERATED

RELEASED

2015 MAR 18

DESIGN		DART AEROSPACE LTD	
DRAWN		HAWKESBURY, ONTARIO, CANADA	
CHECKED	ASS	DRAWING NO.	REV. H
MFG. APPR.		D350-748-241	SHEET 3 OF 4
APPROVED		TITLE	SCALE
DE APPR.		CROSSTUBE (AS 350/355 HI AFT)	NTS
DATE	15.02.25	COPYRIGHT © 2006 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT THE WRITTEN PERMISSION OF DART AEROSPACE LTD.	

DQA: _____ Date: _____




WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
								Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	

Root Cause			FAULT CATEGORY							
Environment ☐	☐	No Re-verification	☐	Pressure/Forced	☐	Temperature/Cure	☐	Power Loss/Surge	☐	Positioned Wrong
Design ☐	☐	Operator	☐	Bending	☐	Set-up	☐	Folio/Program	☐	Outside Dimensions
Doc/Data ☐	☐	Offset/Setup	☐	Centre Not Concentric	☐	BOM/Route	☐	Grain	☐	Over/Under tolerance
Equip/Tooling ☐	☐	Supplier	☐	Cracks	☐	Broken/Damage/Defect	☐	Weld	☐	Part Incorrect
Handling/Pre ☐	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐	Inspection Incomplete/Unqualified	☐	Wrong Stock Pulled	☐	Part Lost/Missing
Material ☐	☐	Use for Testing	☐	Cuffs	☐	Contamination	☐	Out of Sequence	☐	Part Moved
Internal Transport ☐	☐	Poor Information	☐	Crushing	☐	Countersink	☐	Off-set	☐	Drawing
Tribal Knowledge ☐	☐	Rushing	☐	Heat Treat	☐	Cut Too Short	☐	Mislabeled	☐	Finish
LOA ☐	☐	Product Improvement	☐	Wave/Twist in Tube	☐	Instructions Incomplete/Unclear	☐	Fit/Function	☐	Misread
Substation ☐	☐	Process Improvement	☐	Marks/Chatter	☐	Drill Holes	☐	Misaligned/off center	☐	Turning Sequence
Past Expiry Date ☐	☐	Manufacturing Process	OTHER : _____							
Misidentified ☐	☐	Past Due								

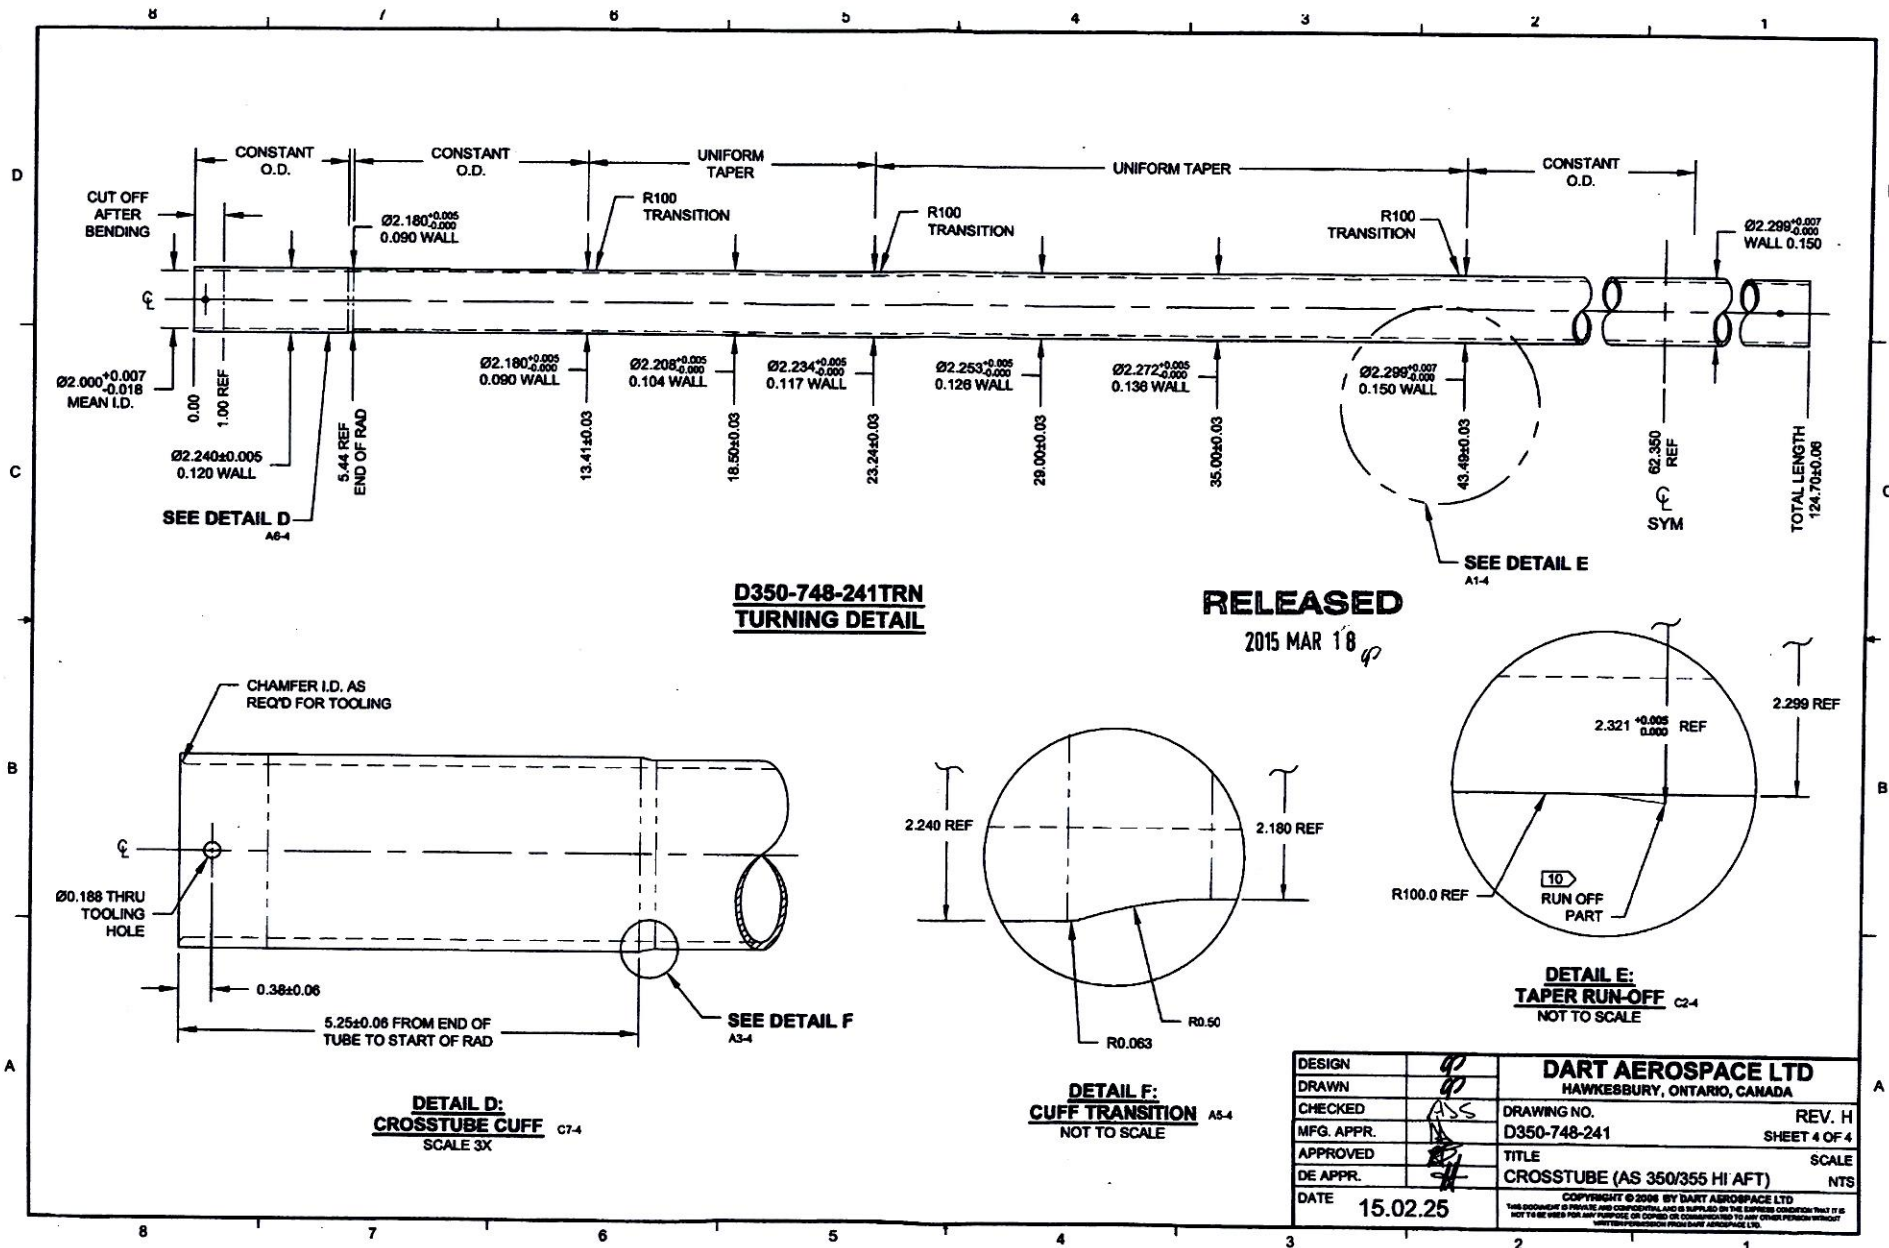

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
							Completed By		
							Lead hand / Supervisor Approval Verification		
							QC / QA Coordinator Approval		

Root Cause				FAULT CATEGORY			
Environment ☐	☐ No Re-verification	☐ Pressure/Forced	☐ Temperature/Cure	☐ Power Loss/Surge	☐ Positioned Wrong		
Design ☐	☐ Operator	☐ Bending	☐ Set-up	☐ Folio/Program	☐ Outside Dimensions		
Doc/Data ☐	☐ Offset/Setup	☐ Centre Not Concentric	☐ BOM/Route	☐ Grain	☐ Over/Under tolerance		
Equip/Tooling ☐	☐ Supplier	☐ Cracks	☐ Broken/Damage/Defect	☐ Weld	☐ Part Incorrect		
Handling/Pre ☐	☐ Training	☐ Crimp/Kink/Ripple/Wave	☐ Inspection Incomplete/Unqualified	☐ Wrong Stock Pulled	☐ Part Lost/Missing		
Material ☐	☐ Use for Testing	☐ Cuffs	☐ Contamination	☐ Out of Sequence	☐ Part Moved		
Internal Transport ☐	☐ Poor Information	☐ Crushing	☐ Countersink	☐ Off-set	☐ Drawing		
Tribal Knowledge ☐	☐ Rushing	☐ Heat Treat	☐ Cut Too Short	☐ Mislabeled	☐ Finish		
LOA ☐	☐ Product Improvement	☐ Wave/Twist in Tube	☐ Instructions Incomplete/Unclear	☐ Fit/Function	☐ Misread		
Substation ☐	☐ Process Improvement	☐ Marks/Chatter	☐ Drill Holes	☐ Misaligned/off center	☐ Turning Sequence		
Past Expiry Date ☐	☐ Manufacturing Process	OTHER : _____					
Misidentified ☐	☐ Past Due						



Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, ON K6A 1K7
Tel: 613 632 9577
Fax: 613 632 1053

PURCHASE ORDER

Purchase Order ID **PO36962**

Purchase Order Date 7/7/2017

PO Print Date 7/7/2017

Page Number 2 of 2

Order From :
METCOR INC.
560 BOUL. ARTHUR SAUVE
SAINT-EUSTACHE, QC J7R 5A8
CA

VC-MET004

Ship To : DART AEROSPACE LTD
1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
CANADA

Contact Name
Vendor Phone 450 473 1884

Ship To Contact
Ship To Phone
Ship Via:
Ship Acct:

Buyer Chantal Lavoie
Customer POID
Customer Tax # 10127-2607
Terms Net 30
Currency CAD
FOB FCA - (Free Carrier)

Line Total: \$0.00

4 163662

D350-748-201
CROSSTUBE

7/10/2017

1.00

\$0.00

\$0.00

Yes

7/10/2017

HEAT TREAT CROSSTUBE AS PER QSI 010 4.3 WITHIN 12HOURS AFTER BENDING

Line Total: \$0.00

5 71401-45

PROCUREMENT
QUALITY CLAUSES

7/10/2017

1.00

\$0.00

\$0.00

No

7/10/2017

Procurement Quality Clauses
A005 right of entry
A021 dart aerospace processing
A024 process certifications
A026 certification of material conformance
A041 QUALITY MANAGEMENT SYSTEM
A042 DART NOTIFICATION BY SUPPLIER
A043 RETENTION OF QUALITY DOCUMENTS

Line Total: \$0.00

PO Total: \$0.00

Note: Terms & Condition of Purchasing(Suppliers) and Procurement Quality Clauses are an integral part of our AS9100 requirements. To learn in detail, please visit www.dartaerospace.com for further explanation.

Change Nbr: 1

Change Date: 7/7/2017

METCOR INC.

560 BOUL. ARTHUR-SAUVÉ
ST-EUSTACHE, QC J7R 5A8
Tel: 450-473-1884 / Fax: 450-491-5498

Reçu de livraison

Delivery Receipt

BON DE TRAVAIL Order	EXPÉDITEUR Shipper ID	BON D'EXPÉDITION Shipper
320419	1	120774

EXPÉDITION COMPLÈTE / Shipped Complete

CLIENT /Customer 215

DART AEROSPACE
1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
Ph: 613-632-5200
Fax: 613-632-1053



LIVRÉ À /Shipped To

DART AEROSPACE
1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
Ph: 613-632-5200
Fax: 613-632-1053

COMMANDE DU CLIENT Customer PO	BON DE LIVRAISON DU CLIENT Customer Shipper No.	TYPE DE MATÉRIEL Material Type	DATE DE LA COMMANDE Order Date	TRANSPORTEUR Carrier
36962		Steel	2017/7/7	client

QUANTITÉ Quantity	No. PIÈCE / Part No.	NOM DE LA PIÈCE / Part Name	DESCRIPTION DE LA PIÈCE Part Description	POIDS Weight
----------------------	-------------------------	--------------------------------	---	-----------------

4 D350-748-101

CROSSTUBE

(1) D350-748-201 163180

(1) D350-748-201 163182

(1) D350-748-201 163181

(1) D350-748-201 163662

1 NIL

120,

8017-710.

TYPE DE CONTENEUR Container Type	# DE CONTENEURS # Of Containers	COMMENTAIRES CONTENEUR Container Comments
NIL	1	

certificat

EMPAQUETAGE Packing	
-------------------------------	--

QUANTITÉ EXPÉDIÉE / Quantity Shipped : 4

POIDS EXPÉDIÉ / Weight Shipped : 120,00

QUANTITÉ RESTANTE / Quantity Remaining : 0

POIDS RESTANT / Weight Remaining : 0,00

certificat

QUANTITÉ EXPÉDIÉE / Quantity Shipped : 4

POIDS EXPÉDIÉ / Weight Shipped : 120,00

Signature:

Date:

EXPÉDIÉ LE / Shipped On : 2017/07/10

METCOR INC.

560 BOUL. ARTHUR-SAUVÉ, ST-EUSTACHE, QC, J7R 5A8

Tél.: 450-473-1884

Télécopieur / Fax administration: 450-491-5498

Télécopieur / Fax production: 450 491-6454

Certificat de Conformité

Certificate of Compliance

BON DE TRAVAIL order	CHARGEMENT load
320419	1

CLIENT / customer 215

DART AEROSPACE

1270 ABERDEEN

HAWKESBURY

ON K8A 1K7

LIVRÉ À / shipped to:

DART AEROSPACE

1270 ABERDEEN

HAWKESBURY

ON K8A 1K7

COMMANDE DU CLIENT customer po	CLASSIFICATION PIECE part classification	MATÉRIEL material	MAÎTRE D'OEUVRE prime contractor	PROGRAM
36962	N/A	Steel		

SPÉCIFICATIONS DU PROCÉDÉ

processing specifications

STRESS REL

SAE AMS 2759/1 REV.E


EXIGENCE / requirement SPÉCIFICATIONS / specified TESTS EXÉCUTÉS / performed RÉSULTATS DE TESTS / results

Visual

QUANTITÉ quantity	POIDS weight	DESCRIPTION DES PIÈCES parts description
4	120	D350-748-101 CROSSTUBE (1) D350-748-201 163180 (1) D350-748-201 163182 (1) D350-748-201 163181 (1) D350-748-201 163662 1 NIL

COMMENTAIRES / comments

APPROUVÉ par / Approved by:



DATE: 2017-07-10

METCOR INC.

560 BOUL. ARTHUR-SAUVÉ, ST-EUSTACHE, QC, J7R 5A8

Tél.: 450-473-1884

Télécopieur / Fax administration: 450-491-5498

Télécopieur / Fax production: 450 491-6454

Certificat de Conformité Détail

Detailed Certificate of Compliance

BON DE TRAVAIL order	CHARGEMENT load
320419	1

CLIENT / customer 215

DART AEROSPACE

1270 ABERDEEN

HAWKESBURY

ON K6A 1K7

LIVRÉ À / shipped to:

DART AEROSPACE

1270 ABERDEEN

HAWKESBURY

ON K6A 1K7

1

COMMANDE DU CLIENT customer po	CLASSIFICATION PIECE part classification	MATÉRIEL material	MAÎTRE D'OEUVRE prime contractor	PROGRAM
36962	N/A	Steel		

SPÉCIFICATIONS DU PROCÉDÉ processing specifications

STRESS REL

SAE AMS 2759/1 REV.E

EXIGENCE / requirement	SPÉCIFICATIONS / specified	TESTS EXÉCUTÉS / performed	RÉSULTATS DE TESTS / results
Visual			

QUANTITÉ quantity	POIDS weight	DESCRIPTION DES PIÈCES parts description
4	120	D350-748-101 CROSSTUBE (1) D350-748-201 163180 (1) D350-748-201 163182 (1) D350-748-201 163181 (1) D350-748-201 163662 1 NIL

COMMENTAIRES / comments

STRESS RELIEF 650F, 2 HRS

Heat treatment (HT) was performed with equipment that meets the requirements of AMS2759 & AMS2750.

All HT operations were in compliance with AMS2759 and all verifications have been performed and documented. No unauthorized changes were performed in regards to the HT. We certify that the material was manufactured, sampled, tested and inspected in accordance with AMS2759 and the purchase order and was found to meet the requirements.

This document and any attached documents may contain confidential or proprietary information and may be subject to export control laws and regulations. If you are not the intended recipient, you are notified that any dissemination, copying of this e-mail and any attachments thereto or use of their contents by any means whatsoever is strictly prohibited. Unauthorized export or re-export is prohibited.

Le traitement thermique (TT) a été fait en utilisant des équipements en conformité avec AMS2759 et AMS 2750.

Le TT a été fait tel que requis par AMS2759 et toutes les vérifications et les tests demandés ont été faites et documentés. Aucun changement n'a été faite par rapport au TT. On certifie que le matériel a été fabriqué, échantillonné, testé et inspecté en accord avec AMS2759 et le bon de commande et le matériel rencontre les exigences spécifiées.

Ce document et les documents qui lui sont joints peuvent contenir des informations confidentielles, être soumis aux réglementations relatives au contrôle des exportations ou ayant un caractère privé. S'ils ne vous sont pas destinés, nous vous signalons qu'il est strictement interdit de les divulguer, de les reproduire ou d'en utiliser de quelque manière que ce soit le contenu. Toute exportation ou réexportation non autorisée est interdite.

APPROUVÉ par / Approved by:

Isabel Otero


Isabel Otero
QA Technician



DATE: 2017-07-11

DART AEROSPACE LTD		Work Order: 163662
Description: Crosstube High Aft (AS350/355)		Part Number: D350-748-201
Inspection Dwg: D350-748-241	Rev: H	Page 1 of 1

Required Dimension	Min	Max
Height	31.10	31.60
1/2 Span	40.77	41.03
Angle	75	77
Total Span	81.54	82.06
Bending Passes	7	--
Crushing	--	8%
Twist	--	0.38

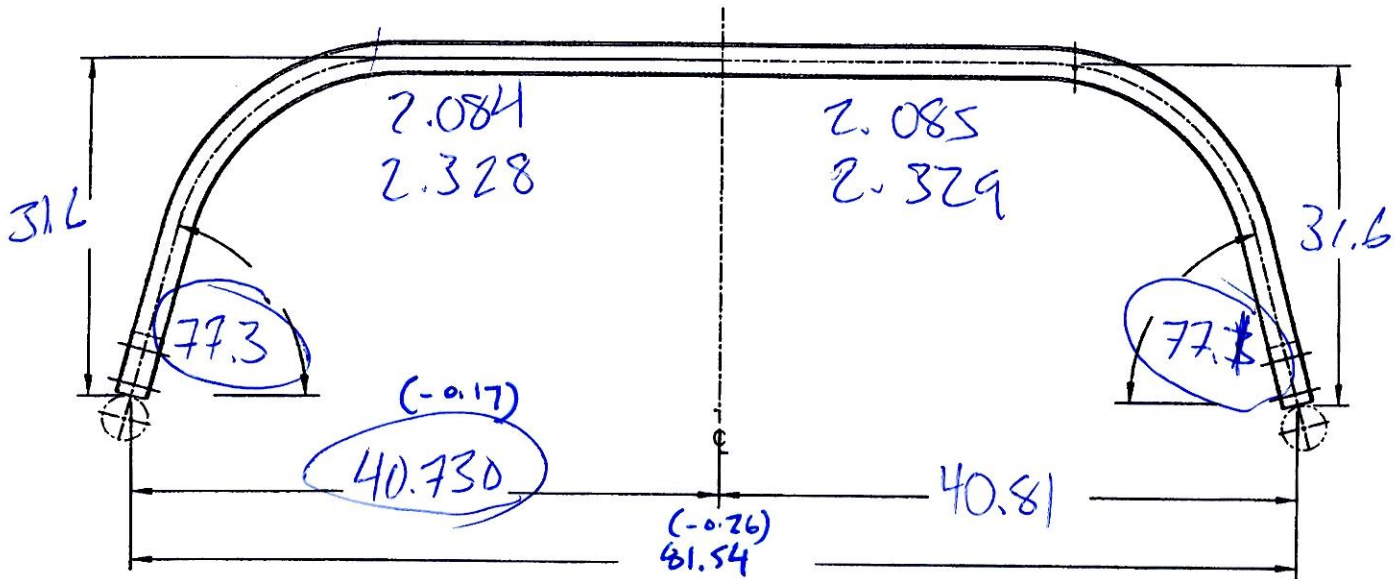

	Side A	Side B
Bending Passes		
Crushing	5.5%	5.5%
Comments		

QC15 Inspection	DAS
Date	38
	9-89
	JUL 13 2017

Rev	Date	Change	Revised by	Approved
A	07.02.06	New Issue	KJ/JM	
B	10.08.23	Dwg Rev updated	KJ	
C	12.04.16	Added bending, crushing & twist dimensions	KJ	
D	12.07.31	Dwg Rev updated	KJ	
E	13.02.27	Dwg Rev updated	KJ	
F	14.02.13	Crushing & twist dimensions revised	KJ	
G	14.11.10	Height dimension revised	KJ	
H	15.07.20	Crushing dimension revised	KJ	



Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, ON K6A 1K7
Tel: 613 632 9577
Fax: 613 632 1053

PURCHASE ORDER

Purchase Order ID **PO37045**

Purchase Order Date 7/13/2017

PO Print Date 7/20/2017

Page Number 6 of 9

Order From : CADORATH COATING 2150 LOGAN AVE. WINNIPEG, MB R2R 0J2 CA	VC-CAD002	Ship To : DART AEROSPACE LTD 1270 ABERDEEN HAWKESBURY, ON K6A 1K7 CANADA
--	-----------	--

Contact Name		Buyer	Diane Baker
Vendor Phone	204 633 9420	Customer POID	
Ship To Contact		Customer Tax #	10127-2607
Ship To Phone		Terms	Net 30
Ship Via:	Journey Freight collect	Currency	CAD
Ship Acct:		FOB	Destination-Collect

11	163661	D350-748-201 Aft Crosstube AS350 / AS355	7/24/2017	1.00	\$803.42	\$803.42
			Yes 7/24/2017			

Stress relief at 375degree for 5hrs
Magnetic Particle Inspect per ASTM E1444
Cad Plate per AMS-QQ-P-416B, Class 1, Type 2
Embrittle relief at 375 degree for 8 hrs, Chromate Treat
C of C req'd

12	163662	D350-748-201 Aft Crosstube AS350 / AS355	7/24/2017	1.00	\$803.42	\$803.42
			Yes 7/24/2017			

Stress relief at 375degree for 5hrs
Magnetic Particle Inspect per ASTM E1444
Cad Plate per AMS-QQ-P-416B, Class 1, Type 2
Embrittle relief at 375 degree for 8 hrs, Chromate Treat
C of C req'd

Line Total: **\$803.42**

Line Total: **\$803.42**

Note:

7/20/2017

Packing Slip

Page 2 of 2



Cadorath Coating

2150 Logan Avenue, Winnipeg, Manitoba R2R-0J2

Phone: (204) 633-9420 Fax: (204) 633-8033

INVOICE NUMBER:

S90743

Net 2% Interest Per Month charged on Overdue Accounts.

Any claims for shortages, overcharges, or damaged goods must be made within seven (7) days from receipt of goods.

Sold To:
Dart Aerospace Ltd.
1270 Aberdeen St.

Hawksbury, ON K6A 1K7

ShipTo:

Customer Order #:	Date Received:	Terms:	G.S.T. #:	Ship Via:	Ship Date:
37045	Jul-18-2017	NET 30 DAYS	10071 6547 RT0001		Jul-24-2017

Item #	Qty	P/N & Description
--------	-----	-------------------

13	1 EA	CROSSTUBE	S/N 163182
		P/N D350-748-201	W/O 172801
14	1 EA	CROSSTUBE	S/N 163658
		P/N D350-748-201	W/O 172802
15	1 EA	CROSSTUBE	S/N 163661
		P/N D350-748-201	W/O 172804
16	1 EA	CROSSTUBE	S/N 163662
		P/N D350-748-201	W/O 172805

SP17-7-25

**CERTIFICATE OF
CONFORMANCE**

**CADORATH PLATING CO. LTD.
2150 LOGAN AVENUE
WINNIPEG, MANITOBA R2J-0J1**

DATE: Jul-24-2017

CONSIGNED TO: Dart Aerospace Ltd.
1270 Aberdeen St.
Hawksbury, ON K6A 1K7

W/O #: 172805

INVOICE #: 90743

**CONTRACT OR
PURCHASE ORDER # 37045**

DESCRIPTION: CROSSTUBE

QTY 1

P/N # D350-748-201

S/N # 163662

STRESS RELIEF BAKE HEAT CHART # 17-631. MPI IAW ASTM-E-1444. CADMIUM PLATE IAW AMS-QQ-P-416C TYPE 2 YELLOW CLASS 1. FINAL MPI IAW ASTM-E-1444. EMBRITTLE RELIEF BAKE HEAT CHART # 17-647.

CERTIFICATE: I certify that the items indicated here on have been inspected and tested and conform to all specifications and requirements detailed on the contract or purchase order.

Approved Inspector:



**skyservice****Work Order Traveler**
Sky Service F.B.O. Inc.

10105 Ryan Avenue, Dorval, Quebec, H9P 1A2

TCCA AMO 53-89 / EASA 145.7142 / BDA AMO 385

WO #: MWO32771	Customer: Dart Aerospace Ltd.	Dept: NDT YUL	Reference: WILL FOLLOW
Descr:	PN:	S/N:	Qty: 1
Make:	Model:	Reg:	A/C S/N:
TSN:	CSN:	TSO:	
Task: UNSCHEDULED			Sequence: 1

Work Required:


CARRY OUT NDT INSPECTION (LIQUID PENETRANT) ON 13 CROSSTUBES

ITEM ID: D350-748-201 AFT CROSSTUBE AS350 / AS355 (QTY7)


- 1 - WORK ORDER ID#: 161645
- 2 - WORK ORDER ID#: 161647
- 3 - WORK ORDER ID#: 163658
- 4 - WORK ORDER ID#: 163661
- 5 - WORK ORDER ID#: 163662
- 6 - WORK ORDER ID#: 163180
- 7 - WORK ORDER ID#: 163182

ITEM ID: D350-748-101 FWD CROSSTUBE AS350 / AS355 (QTY6)

- 8 - WORK ORDER ID#: 163665
- 9 - WORK ORDER ID#: 163183
- 10 -WORK ORDER ID#: 163184
- 11- WORK ORDER ID#: 163185
- 12 -WORK ORDER ID#: 163186
- 13 -WORK ORDER ID#: 163188

Action Taken:	Date:	Initial/Stamp:				
LIQUID PENETRANT INSPECTION CARRIED OUT ON ITEMS LISTED ABOVE (ITEMS 1-13) AS PER ASTM1417M-13 NO CRACK FOUND Pen: ZL-27A MWO5678 DEV: SKD-S2 MPO11715 CLEANER: SKC-S MPO13923	JUL 25 2017	DOT-APP 61 53-89 				
Description	Location	P/N	Qty	Batch	S/N Off	S/N On
						

I certified that the maintenance described above has been performed in accordance with the applicable standard of airworthiness.

Signature: 	ACA/SCA Stamp DOT-APP 61 53-89	Date: JUL 25 2017
Name: ANTONINO MARCHETTA		



Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, ON K6A 1K7
Tel: 613 632 9577
Fax: 613 632 1053

PURCHASE ORDER

Purchase Order ID **PO37211**

Purchase Order Date 7/25/2017

PO Print Date 7/25/2017

Page Number 1 of 5

Order From :
SKYSERVICE
6120 MIDFIELD ROAD
MISSISSAUGA, ONTARIO L5P 1B1
CANADA

VC-SKY001

Ship To : DART AEROSPACE LTD
1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
CANADA

Contact Name
Vendor Phone 905-678-5636

Ship To Contact
Ship To Phone
Ship Via: Delivered
Ship Acct:

Buyer
Customer POID
Customer Tax # 10127-2607
Terms Net 30
Currency CAD
FOB FCA - (Free Carrier)

Line Nbr	Reference Vendor Part Number Line Comments Delivery Comments	Description/ Mfg ID	Req Date/ Taxable Promise Date	CD	Req Qty/ Unit of Measure	PO Unit Price	Extended Price
2	161645 ✓ LPI PER QSI038 4.1	D350-748-201	7/25/2017 Yes 7/25/2017		1.00	\$300.00	\$300.00
						Line Total:	\$300.00
3	161647 ✓ LPI PER QSI038 4.1	D350-748-201	7/25/2017 Yes 7/25/2017		1.00	\$300.00	\$300.00
						Line Total:	\$300.00
4	163658 ✓ LPI PER QSI038 4.1	D350-748-201	7/25/2017 Yes 7/25/2017		1.00	\$300.00	\$300.00

Note:

7/25/2017



Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, ON K6A 1K7
Tel: 613 632 9577
Fax: 613 632 1053

PURCHASE ORDER

Purchase Order ID **PO37211**

Purchase Order Date 7/25/2017

PO Print Date 7/25/2017

Page Number 2 of 5

Order From :
SKYSERVICE
6120 MIDFIELD ROAD
MISSISSAUGA, ONTARIO L5P 1B1
CANADA

VC-SKY001

Ship To : DART AEROSPACE LTD
1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
CANADA

Contact Name
Vendor Phone 905-678-5636

Ship To Contact
Ship To Phone
Ship Via: Delivered
Ship Acct:

Buyer Diane Baker
Customer POID
Customer Tax # 10127-2607
Terms Net 30
Currency CAD
FOB FCA - (Free Carrier)

Line Total: **\$300.00**

5	163661 ✓	D350-748-201	7/25/2017 Yes 7/25/2017	1.00	\$300.00	\$300.00
---	----------	--------------	-------------------------------	------	----------	----------

LPI PER QSI038 4.1

Line Total: **\$300.00**

6	163662 ✓	D350-748-201	7/25/2017 Yes 7/25/2017	0.00	\$300.00	\$0.00
---	----------	--------------	-------------------------------	------	----------	--------

LPI PER QSI038 4.1

Line Total: **\$0.00**

7	163180 ✓	D350-748-201	7/25/2017 Yes 7/25/2017	1.00	\$300.00	\$300.00
---	----------	--------------	-------------------------------	------	----------	----------

LPI PER QSI038 4.1

Line Total: **\$300.00**

Note:

7/25/2017



Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, ON K6A 1K7
Tel: 613 632 9577
Fax: 613 632 1053

PURCHASE ORDER

Purchase Order ID **PO37211**

Purchase Order Date 7/25/2017

PO Print Date 7/25/2017

Page Number 3 of 5

Order From :
SKYSERVICE
6120 MIDFIELD ROAD
MISSISSAUGA, ONTARIO L5P 1B1
CANADA

VC-SKY001

Ship To : DART AEROSPACE LTD
1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
CANADA

Contact Name

Vendor Phone

905-678-5636

Ship To Contact

Ship To Phone

Ship Via:

Delivered

Ship Acct:

Buyer

Diane Baker

Customer POID

Customer Tax #

10127-2607

Terms

Net 30

Currency

CAD

FOB

FCA - (Free Carrier)

8	163182	D350-748-201	7/25/2017 Yes 7/25/2017	1.00	\$300.00	\$300.00
LPI PER QSI038 4.1						
						Line Total: \$300.00
9	163665	D350-748-101	7/25/2017 Yes 7/25/2017	1.00	\$300.00	\$300.00
LPI PER QSI038 4.1						
						Line Total: \$300.00
10	163183	D350-748-101	7/25/2017 Yes 7/25/2017	1.00	\$300.00	\$300.00
LPI PER QSI038 4.1						
						Line Total: \$300.00

Note:

7/25/2017



Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, ON K6A 1K7
Tel: 613 632 9577
Fax: 613 632 1053

PURCHASE ORDER

Purchase Order ID PO37211

Purchase Order Date 7/25/2017

PO Print Date 7/25/2017

Page Number 4 of 5

Order From :
SKYSERVICE
6120 MIDFIELD ROAD
MISSISSAUGA, ONTARIO L5P 1B1
CANADA

VC-SKY001

Ship To : DART AEROSPACE LTD
1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
CANADA

Contact Name

Vendor Phone

905-678-5636

Ship To Contact

Ship To Phone

Ship Via:

Ship Acct:

Delivered

Buyer

Customer POID

Customer Tax #

Terms

Currency

FOB

Diane Baker

10127-2607

Net 30

CAD

FCA - (Free Carrier)

11	163184	✓	D350-748-101	7/25/2017 Yes 7/25/2017	1.00	\$300.00	\$300.00
LPI PER QSI038 4.1							
							Line Total: \$300.00
12	163185	✓	D350-748-101	7/25/2017 Yes 7/25/2017	1.00	\$300.00	\$300.00
LPI PER QSI038 4.1							
							Line Total: \$300.00
13	163186	✓	D350-748-101	7/25/2017 Yes 7/25/2017	1.00	\$300.00	\$300.00
LPI PER QSI038 4.1							
							Line Total: \$300.00

Note:

7/25/2017



Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, ON K6A 1K7
Tel: 613 632 9577
Fax: 613 632 1053

PURCHASE ORDER

Purchase Order ID **PO37211**

Purchase Order Date 7/25/2017

PO Print Date 7/25/2017

Page Number 5 of 5

Order From :
SKYSERVICE
6120 MIDFIELD ROAD
MISSISSAUGA, ONTARIO L5P 1B1
CANADA

VC-SKY001

Ship To : DART AEROSPACE LTD
1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
CANADA

Contact Name
Vendor Phone 905-678-5636

Ship To Contact
Ship To Phone
Ship Via: Delivered
Ship Acct:

Buyer Diane Baker
Customer POID
Customer Tax # 10127-2607
Terms Net 30
Currency CAD
FOB FCA - (Free Carrier)

14	163188	D350-748-101	7/25/2017	1.00	\$300.00	\$300.00
			Yes			
			7/25/2017			
		LPI PER QSI038 4.1				

Line Total: \$300.00

15	71401-45	procurement quality clauses	7/25/2017	1.00	\$0.00	\$0.00
			No			
			7/25/2017			
		Procurement Quality Clauses				
		A005 right of entry				
		A012 chemical and physical test report				
		A016 personnel qualification				
		A017 raw material identification (as applicable)				
		A024 process certifications				
		A026 certification of material conformance				
		A041 quality management system				
		A042 dart notification by supplier				
		A043 retention of quality documents				

Line Total: \$0.00

PO Total: \$3,600.00

Note: Terms & Condition of Purchasing(Suppliers) and Procurement Quality Clauses are an integral part of our AS9100 requirements. To learn in detail, please visit www.dartaerospace.com for further explanation.

Change Nbr: 4

Change Date: 7/25/2017

Wednesday, July 05, 2017 10:24:02 AM

Page 1

****VERIFY CROSSTUBE DIMENSIONS AS PER DWG****

DAS
5
9-89

JUL 28 2017



Department of Transport

Supplemental Type Certificate

This approval is issued to:

Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, Ontario
Canada K6A 1K7

Number: SH06-27

Issue No.: 2

Approval Date: August 16, 2006

Issue Date: July 27, 2010

Responsible Office:

Prairie and Northern

Aircraft/Engine Type or Model:

EUROCOPTER FRANCE AS 350 B, B1, B2, B3, BA, D, D1
EUROCOPTER FRANCE AS 355 E, F, F1, F2, N, NP

Canadian Type Certificate or Equivalent:

EUROCOPTER FRANCE AS 350 Series: H-83
EUROCOPTER FRANCE AS 355 Series: H-87

Description of Type Design Change:

Crosstube Installation

**Installation/Operating Data,
Required Equipment and Limitations:**

Manufacture of the Crosstube Installation must be in accordance with Dart Aerospace Ltd. MDL-D350-748, Revision F, dated 2010-06-30, or later Transport Canada approved revision.


Installation of the Crosstube Installation must be in accordance with Dart Aerospace Ltd. IIN-D350-748, Revision B, dated 2007-06-15, or later Transport Canada approved revision.

Maintenance of the Crosstube Installation must be in accordance with Transport Canada accepted Dart Aerospace Ltd. ICA-D350-748, Revision 1, dated 2010-06-29, or later accepted revision.


Basis of Certification:

The basis of certification for this modification is FAR 27, up to and including Amendment 27-40 for the affected areas.

— End —



Conditions: This approval is only applicable to the type/model of aeronautical product specified therein. Prior to incorporating this modification, the installer shall establish that the interrelationship between this change and any other modification(s) incorporated will not adversely affect the airworthiness of the modified product.


Greg Oucharek
For Minister of Transport

Canada
